

BIM-Linked Construction Progress and Schedule Deviation Dashboard

IFC Class

Select IFC Class

All

Construction Activity

Select Activity

All

Progress Status

Select Status

All

Planned Event Records

7166

Observed Event Records

3661

Late Event Records

194

Record Coverage %

51.09%

Element Coverage %

67.28%

Planned Elements

3505

Delayed Elements

119

Observed Elements




2358

Late Record Rate %

5.30%

Observed Element Delay Rate %

5.05%

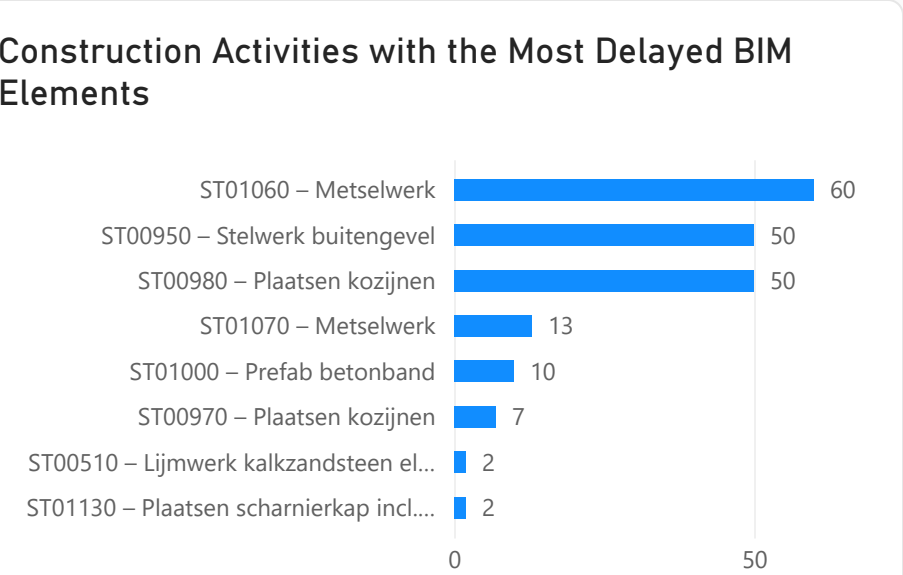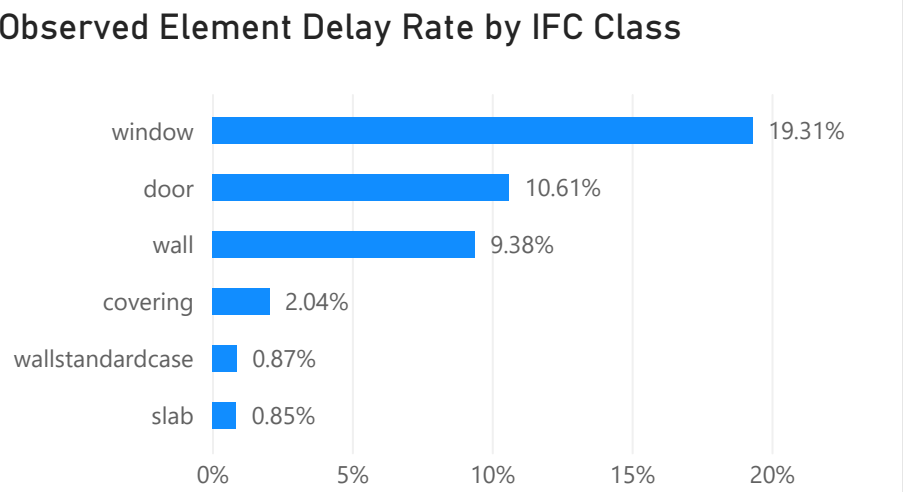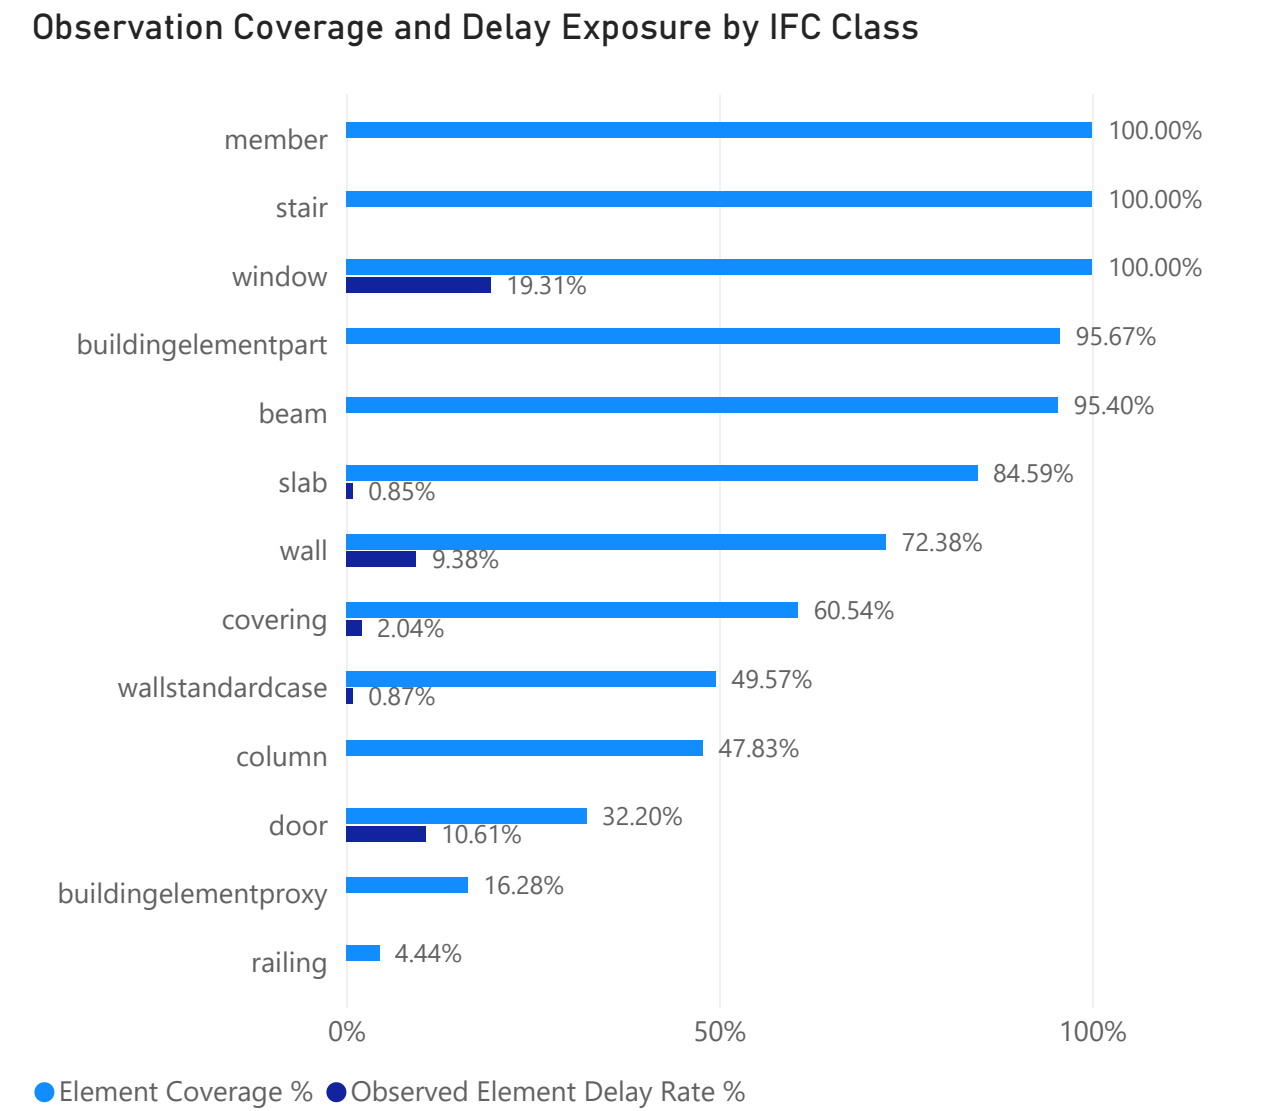

Delayed Construction Activity Details					
Task Label	Planned_Start	Planned_Finish	Observed Elements	Delayed Elements	Observed Element Delay Rate %
ST01060 – Metselwerk	2015-07-09	2015-07-21	527	60	11.39%
ST00950 – Stelwerk buitengevel	2015-07-02	2015-07-08	171	50	29.24%
ST00980 – Plaatsen kozijnen	2015-07-06	2015-07-10	171	50	29.24%
ST01070 – Metselwerk	2015-07-22	2015-08-04	199	13	6.53%
ST01000 – Prefab betonband	2015-08-17	2015-08-18	84	10	11.90%
ST00970 – Plaatsen kozijnen	2015-06-18	2015-06-24	176	7	3.98%
ST00510 – Lijmwerk kalkzandsteen elementen	2015-06-19	2015-06-23	19	2	10.53%
ST01130 – Plaatsen scharnierkap incl. goot en platte daken	2015-08-28	2015-09-17	313	2	0.64%
Total			1222	119	9.74%
